
# Roof Report

Oct 19, 2022

YOUR LOGO

***Prepared by:***
My Company
555 Company Rd
Jackson,  TX 73344
info@mycompany.com
(888) 555-1234

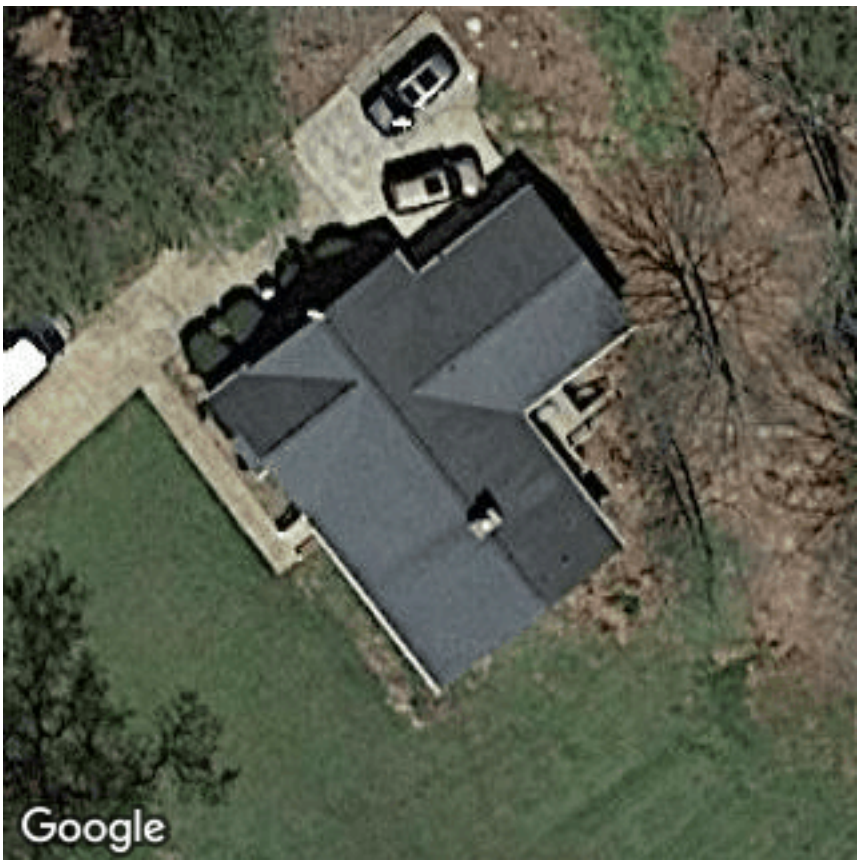


1934 Natalie Drive, Bethlehem, GA 30620
Claim# 110478573906

Powered by PG Reports™
©2022 Pitch Gauge LLC

## Estimator Info

| | |
|---|---|
| Data Input By: | My Company<br>555 Company Rd<br>Jackson,  TX 73344 |
| Project Manager: | Tim Jacobs |
| Email: | info@mycompany.com |
| Mobile: | (888) 555-1234 |

## Client Info

| | |
|---|---|
| Name: | Jamie Taylor |
| Site Address: | 1934 Natalie Drive<br>Bethlehem, GA 30620 |
| Phone: | (678) 577-1234 |
| Mobile: | (678) 577-1235 |
| Email: | jamie@exmaple.com |

## Policy Info

| | |
|---|---|
| Policy Number: | HVY59394 |
| Claim Number: | 110478573906 |
| Damage Type: | Wind |
| Damage Date: | May 06, 2022 |

## Insurance Info

| | |
|---|---|
| Insurance Company: | Home Insurance |
| Main Phone: | 1 (800) 235-1234 |
| Fax: | 1 (800) 235-1235 |

©2022 Pitch Gauge LLC


My Company
info@mycompany.com
(888) 555-1234

Claim# 110478573906

1934 Natalie Drive, Bethlehem, GA 30620

# Pitch Breakdown

(4/12) 632.81 ft²
(6/12) 841.52 ft²
(7/12) 1,155.83 ft²
(8/12) 329.7 ft²

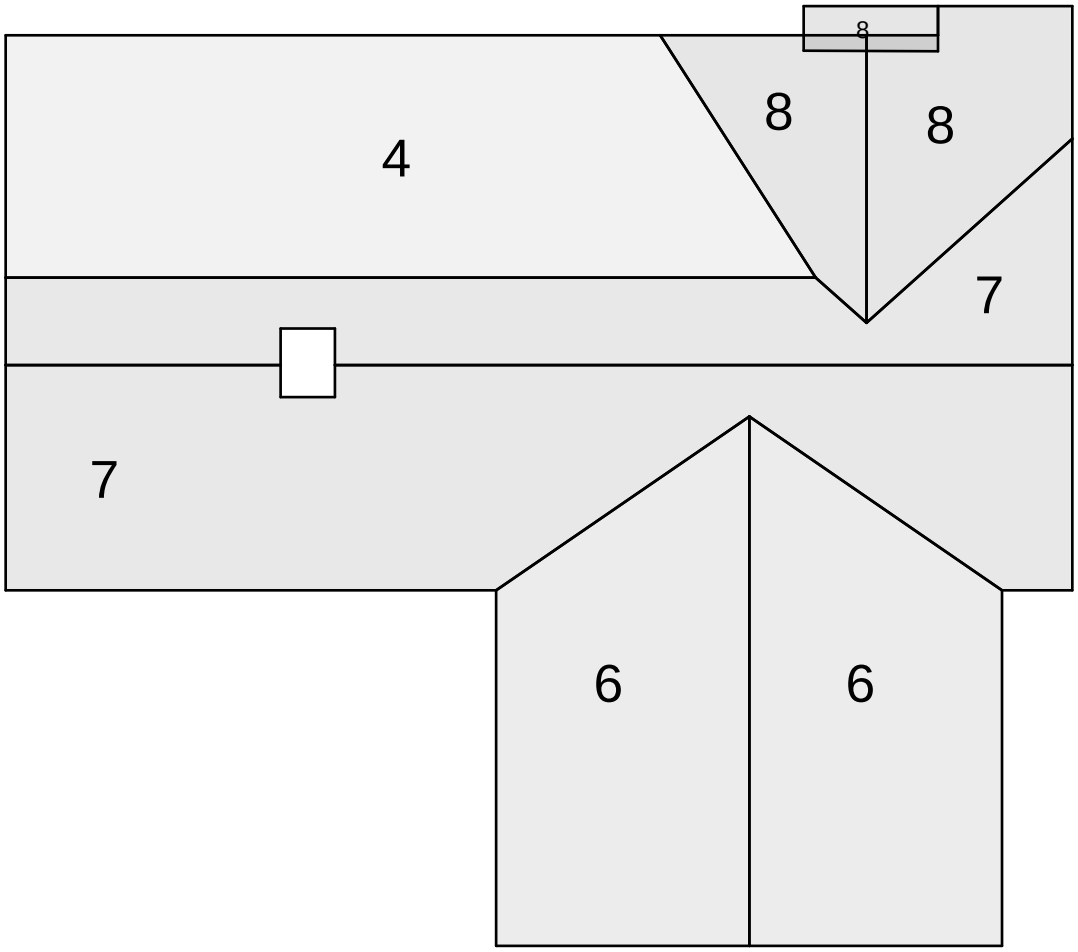


©2022 Pitch Gauge LLC


My Company
info@mycompany.com
(888) 555-1234

Claim# 110478573906

1934 Natalie Drive, Bethlehem, GA 30620

# Area Breakdown

29.6 SQs

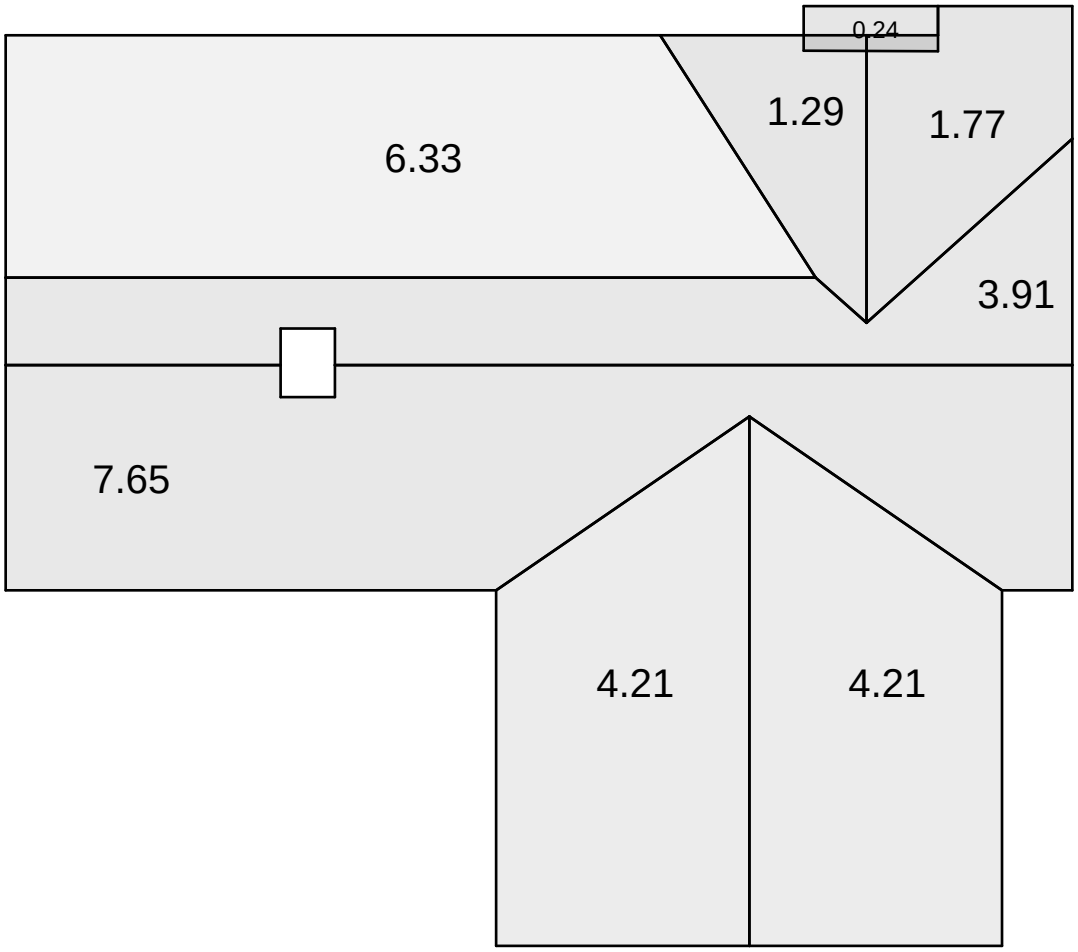



©2022 Pitch Gauge LLC

My Company
info@mycompany.com
(888) 555-1234

Claim# 110478573906

1934 Natalie Drive, Bethlehem, GA 30620

# Length Breakdown

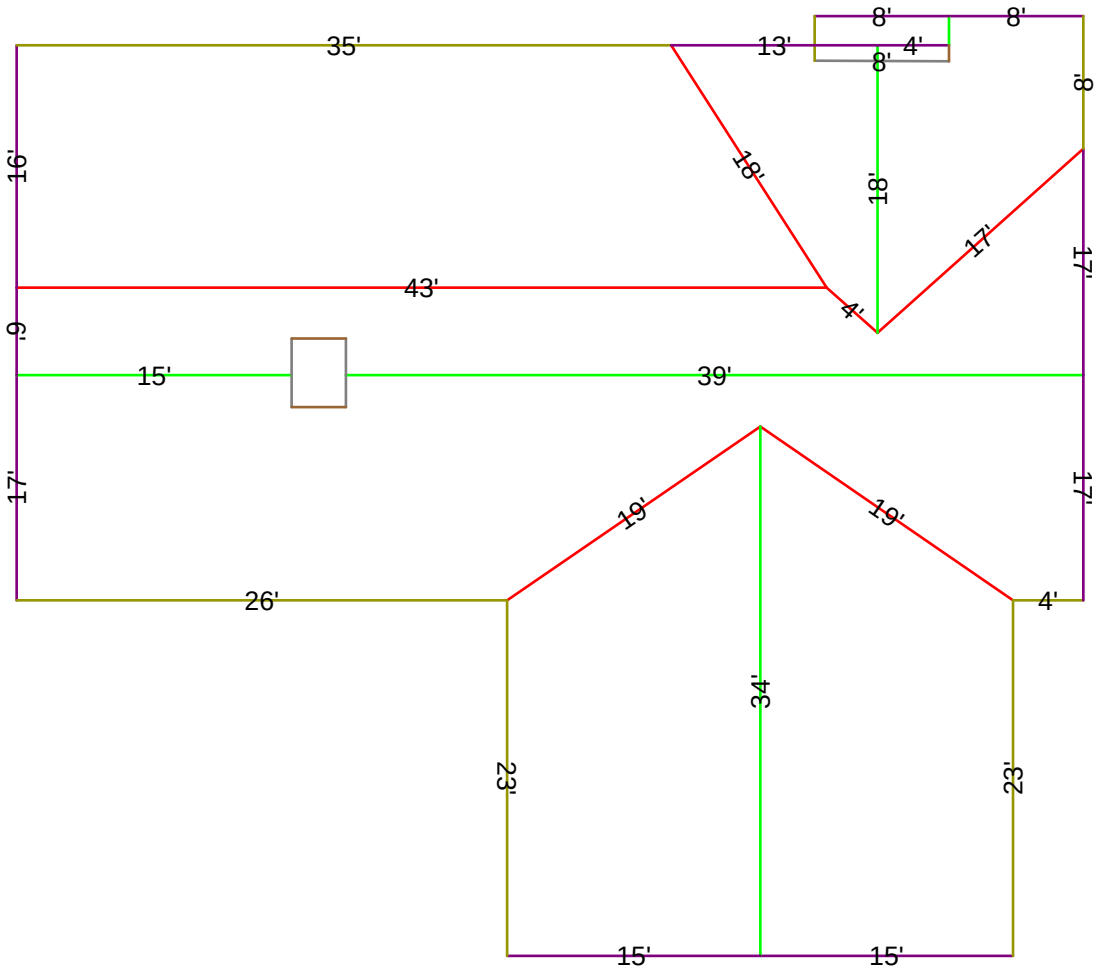


| | | | |
|---|---|---|---|
| Ridges: | 107ft 8in | Wall Flashing: | 6ft 8in |
| Eaves: | 121ft 2in | Step Flashing: | 18ft 6in |
| Rakes: | 136ft 9in | Gutters: | 0ft 0in |
| Valleys: | 120ft 1in | Unknown: | 0ft 0in |
| Hips: | 0ft 0in | | |

©2022 Pitch Gauge LLC


My Company
info@mycompany.com
(888) 555-1234

Claim# 110478573906

1934 Natalie Drive, Bethlehem, GA 30620

## Totals

| | |
|---|---|
| Ridges: | 107ft 8in |
| Eaves: | 121ft 2in |
| Rakes: | 136ft 9in |
| Valleys: | 120ft 1in |
| Hips: | 0ft 0in |
| Wall Flashing: | 6ft 8in |
| Step Flashing: | 18ft 6in |
| Gutters: | 0ft 0in |
| Unknown: | 0ft 0in |
| **Tear Off:** | 29.60 SQs (2,959.86 ft²) |
| Project Waste: | 12% |
| **Total Squares:** | 33.15 SQs (3,315.04 ft²) |

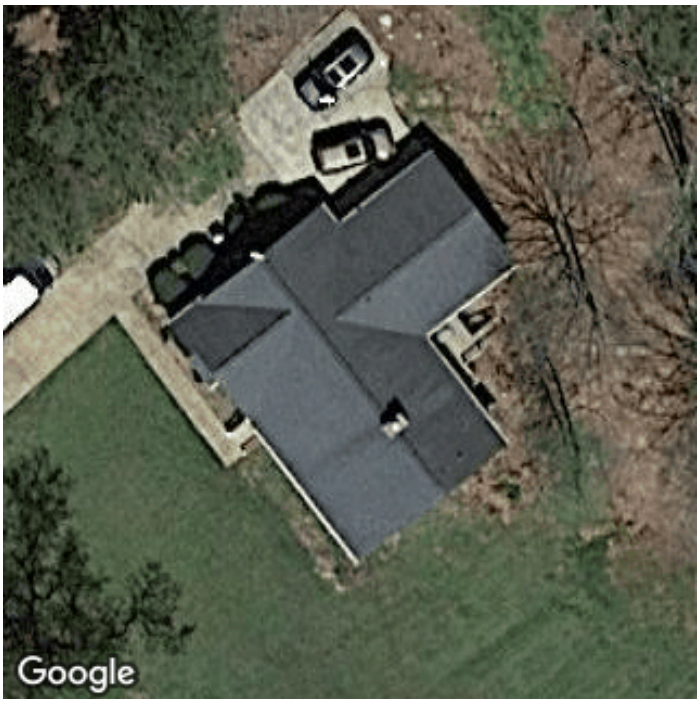


| Waste Factor | 5% | 10% | 12% | 15% | 18% | 20% | 22% | 25% |
|---|---|---|---|---|---|---|---|---|
| Total Squares | 31.08 | 32.56 | 33.15 | 34.04 | 34.93 | 35.52 | 36.11 | 37.00 |
| Total Area ft² | 3,107.85 | 3,255.85 | 3,315.04 | 3,403.84 | 3,492.63 | 3,551.83 | 3,611.03 | 3,699.83 |

©2022 Pitch Gauge LLC
